



Construction Update

BO 1444(60) Hartford

[Hartford Bridge #7 Replacement Project]


DATE: Friday, July 21, 2023

TRAFFIC IMPACT AND DURATION: The closure of VT Route 14 (VT 14) continues between Ferry Crossing Road and Christian Street. This 60-day road closure will detour traffic along a signed route on the VA Cut Off Road, Mill Road, U.S. Route 4/5 and VT 14. Pedestrian and bicycle access will be maintained through the closure area.

No other traffic impacts are expected throughout the project limits between Monday, July 24 and Friday, July 28.

CONSTRUCTION ACTIVITIES: Crews will continue drainage work. Waterline work will begin after drainage is complete. Pile driving for abutment 2 will continue. Drilled shaft foundation work may resume this week if the river level recedes enough to continue work.

The recent storm caused damage to the causeway that was installed to facilitate construction activities. Crews are reconstructing the causeway now that the water has receded. While the storm set the project back by 2-3 weeks, the new bridge is still planned to reopen in late 2024.

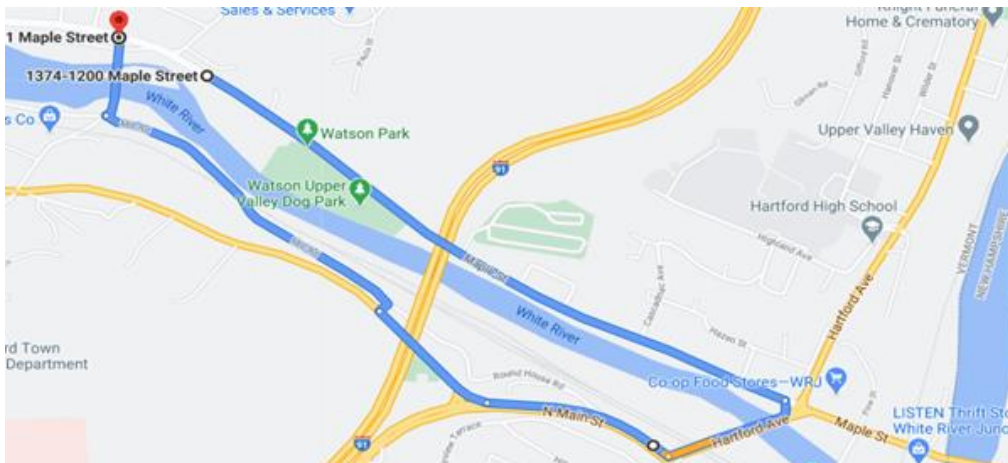

LOCATION: The Hartford BO 1444(60) project is a full bridge replacement and realignment (at Christian Street) of bridge #7 over the White River and Town Highway 98.

PROJECTED COMPLETION: Fall 2025

[VTrans Project Factsheet](#)

Contact Us!

Public Information Consultant: Delia Makhetha

Project Hotline: 802-496-8963

Email: info@hartfordvtprojects.com

Town of Hartford



VTrans

